
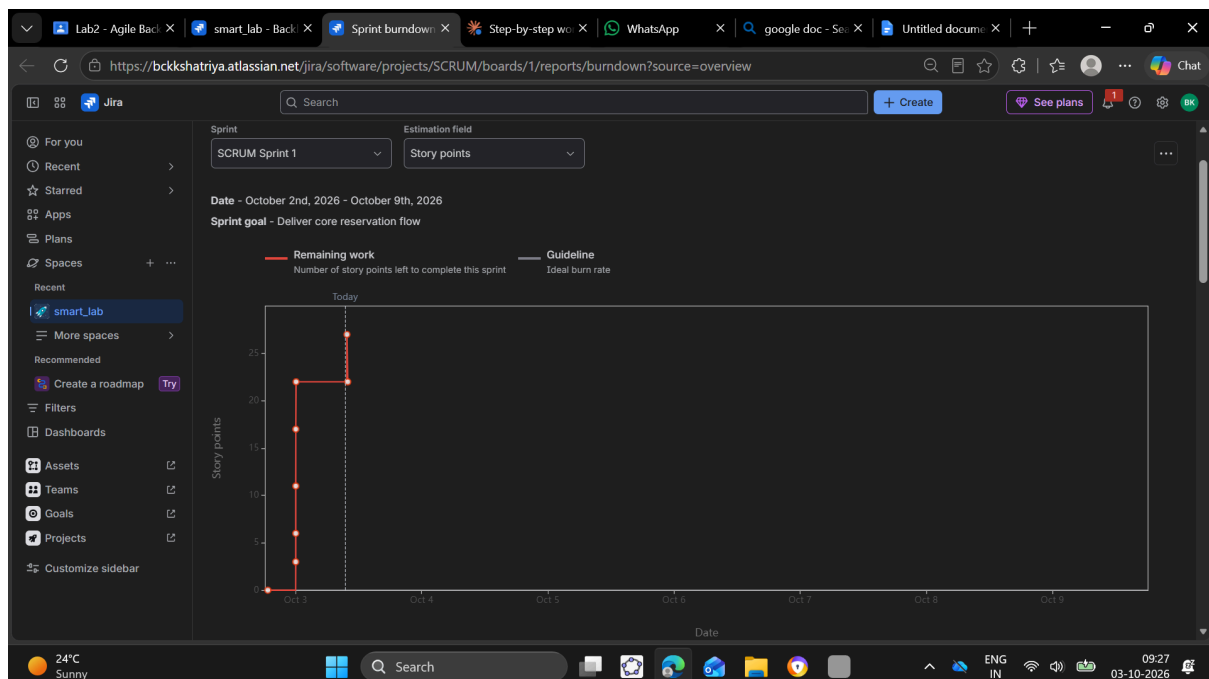


Name-Bhoomika Kshatriya
srn-PES1UG24AM068

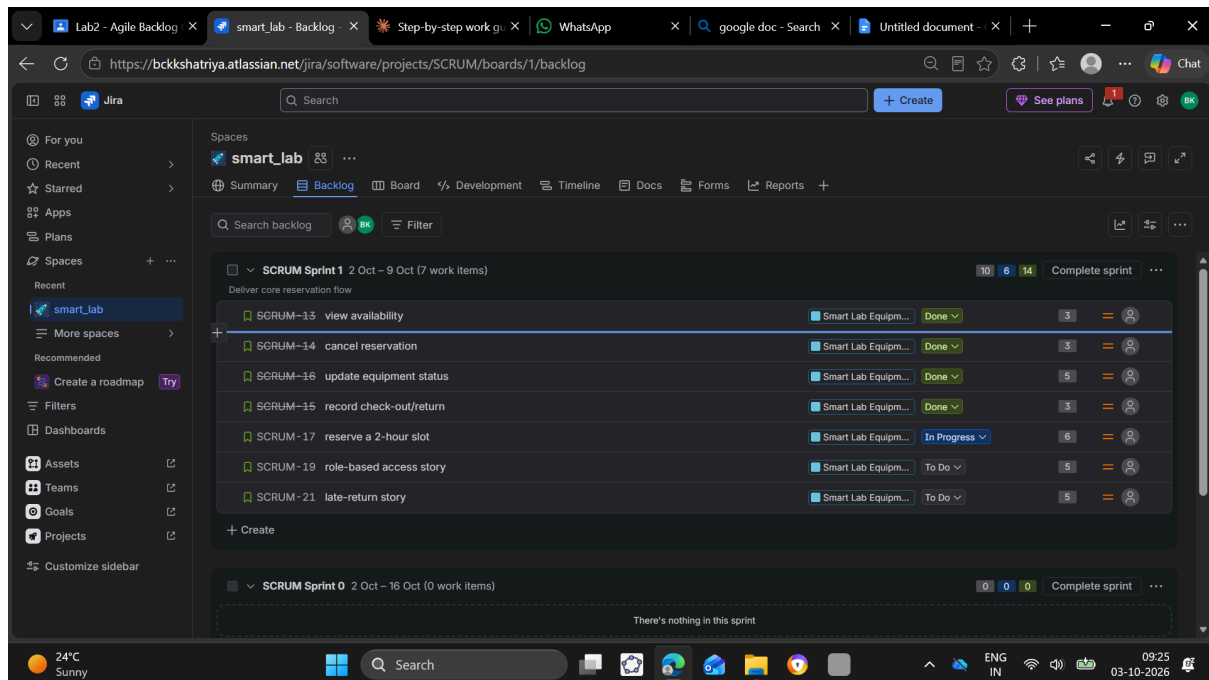

1. Did your estimations reflect the actual effort?

Partly. I used Fibonacci points and gave the highest values to the reservation story (6) and the equipment status and late-return stories (5), because they involve locking, validation and business rules. The simple stories (view availability, cancel, record return) at 3 points each moved through the board quickly, which matched the estimates. Since this was a simulation with no real development time, I can't fully validate the estimates, but in a real sprint I'd expect the concurrency handling in the reservation story to take longer than 6 points suggests.

2. Was your backlog well-prioritized?

Mostly yes. I ordered the stories around the core flow first: view availability, reserve, cancel, then technician features (status, check-out/return, late flags) and role-based access last. Reservation depends on equipment status being correct, so in hindsight "update equipment status" should have been prioritized above cancel. Role-based access is a cross-cutting requirement, so I'd move it earlier in a real project.

3. How did your simulated sprint align with your plan?

The plan was 30 story points across 7 stories in a one-week sprint. The sprint ran roughly as planned, with 3 stories completed first, then work moving through In Progress and In Review. However, some stories were added after the sprint started, which raised the total scope and made the burndown rise at the start instead of falling. This showed me how scope change affects a sprint, and that the backlog should be finalized before starting it.

4. What insights did the burndown chart give about your team's capacity?

The chart showed the team completing about 14 points in the first stretch ($3 + 3 + 3 + 5$), against the ideal line. This suggests a capacity of roughly 14 to 15 points per sprint, so 30 points was over-committed, and a realistic plan would be about 15 points. It also showed that the scope increase at the start made the sprint look behind from day one. Next time I'd size the sprint to the team's observed velocity and avoid mid-sprint additions.
